

Wahoo Middle-High School Addition & Improvements

Monthly Progress Update

3/27/2024

Progress Update:

1. Middle-High School Addition

a. Completed

- i. Interior framing Area G 1st & 2nd floor Classrooms
- ii. Gymnasium concrete slab poured
- iii. Corridor F101 concrete slab poured
- iv. Commons area concrete stair landing and seating poured
- v. Commons Stairs erected
- vi. Mechanical in-wall/overhead rough-ins (2nd floor)
- vii. Electrical in-wall/overhead rough-ins (2nd floor)
- viii. Plumbing/Fire Sprinkler in-wall/overhead rough-ins (2nd floor)
- ix. Installation of translucent panel glass in the Gymnasium
- x. Setting of door frames
- xi. Installation of RTU curbs
- xii. Roofing installation – 98% complete

b. On-Going


- i. Exterior brick wall assembly
- ii. Setting aluminum frames and windows in the clerestory
- iii. Mechanical in-wall/overhead rough-ins (1st floor)
- iv. Electrical in-wall/overhead rough-ins (1st floor)
- v. Plumbing/Fire Sprinkler in-wall/overhead rough-ins (1st floor)
- vi. Drywall installation – 2nd floor Area G
- vii. Misc. curbs and roof detailing
- viii. Interior precast touch-up
- ix. Misc. concrete stoops/paving

c. Upcoming:

- i. Commons area railing system
- ii. Exterior precast touch-ups
- iii. Drywall installation – 1st floor Area G





Exterior/Interior of Labs

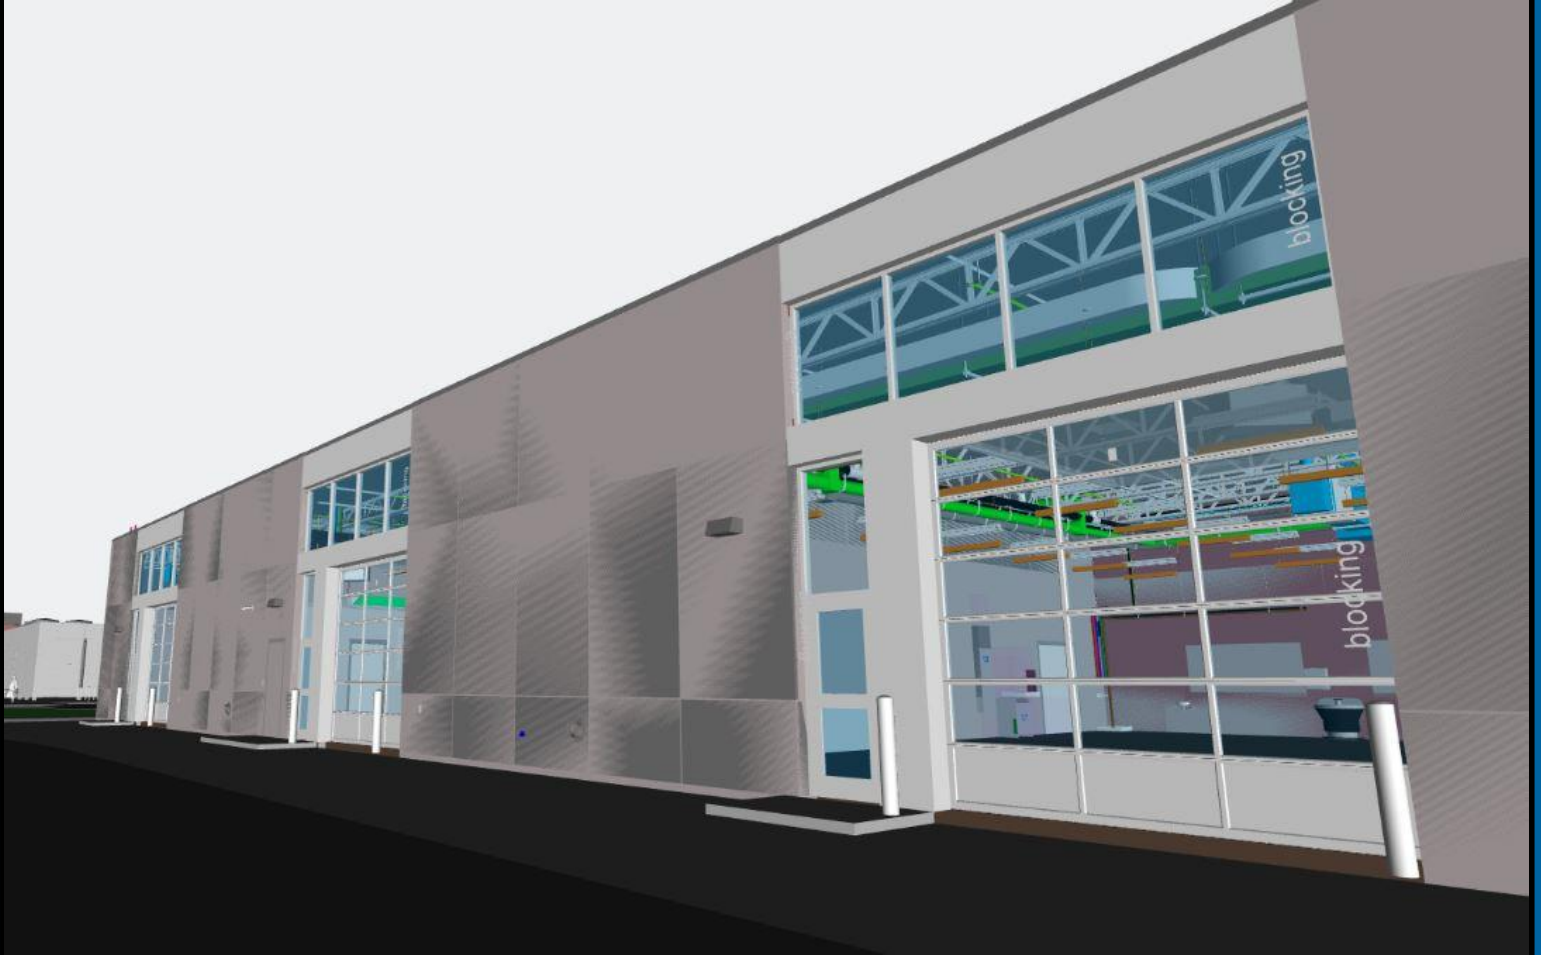



Translucent Glass Panels @ Gymnasium

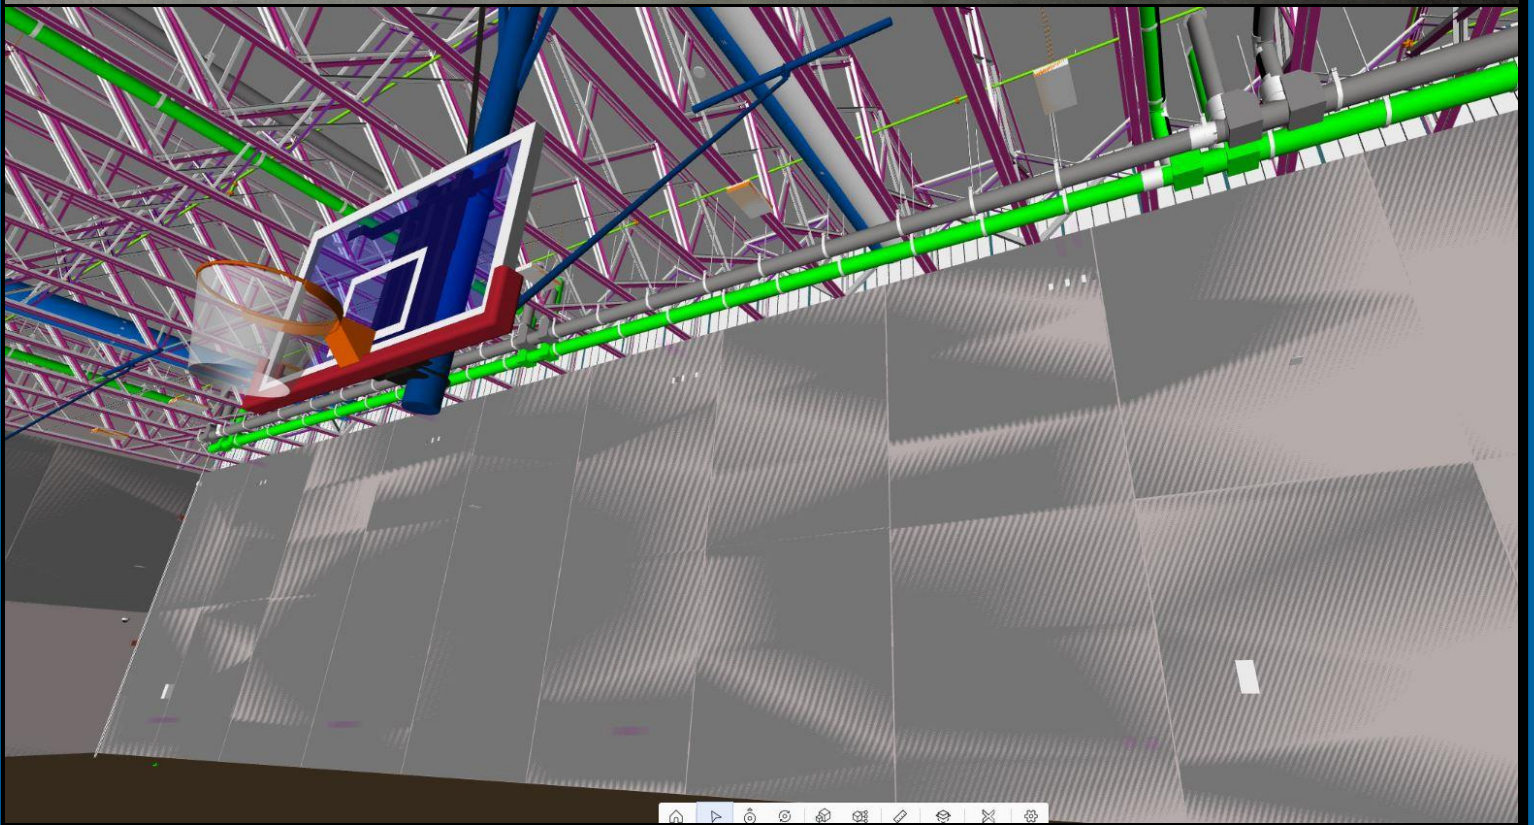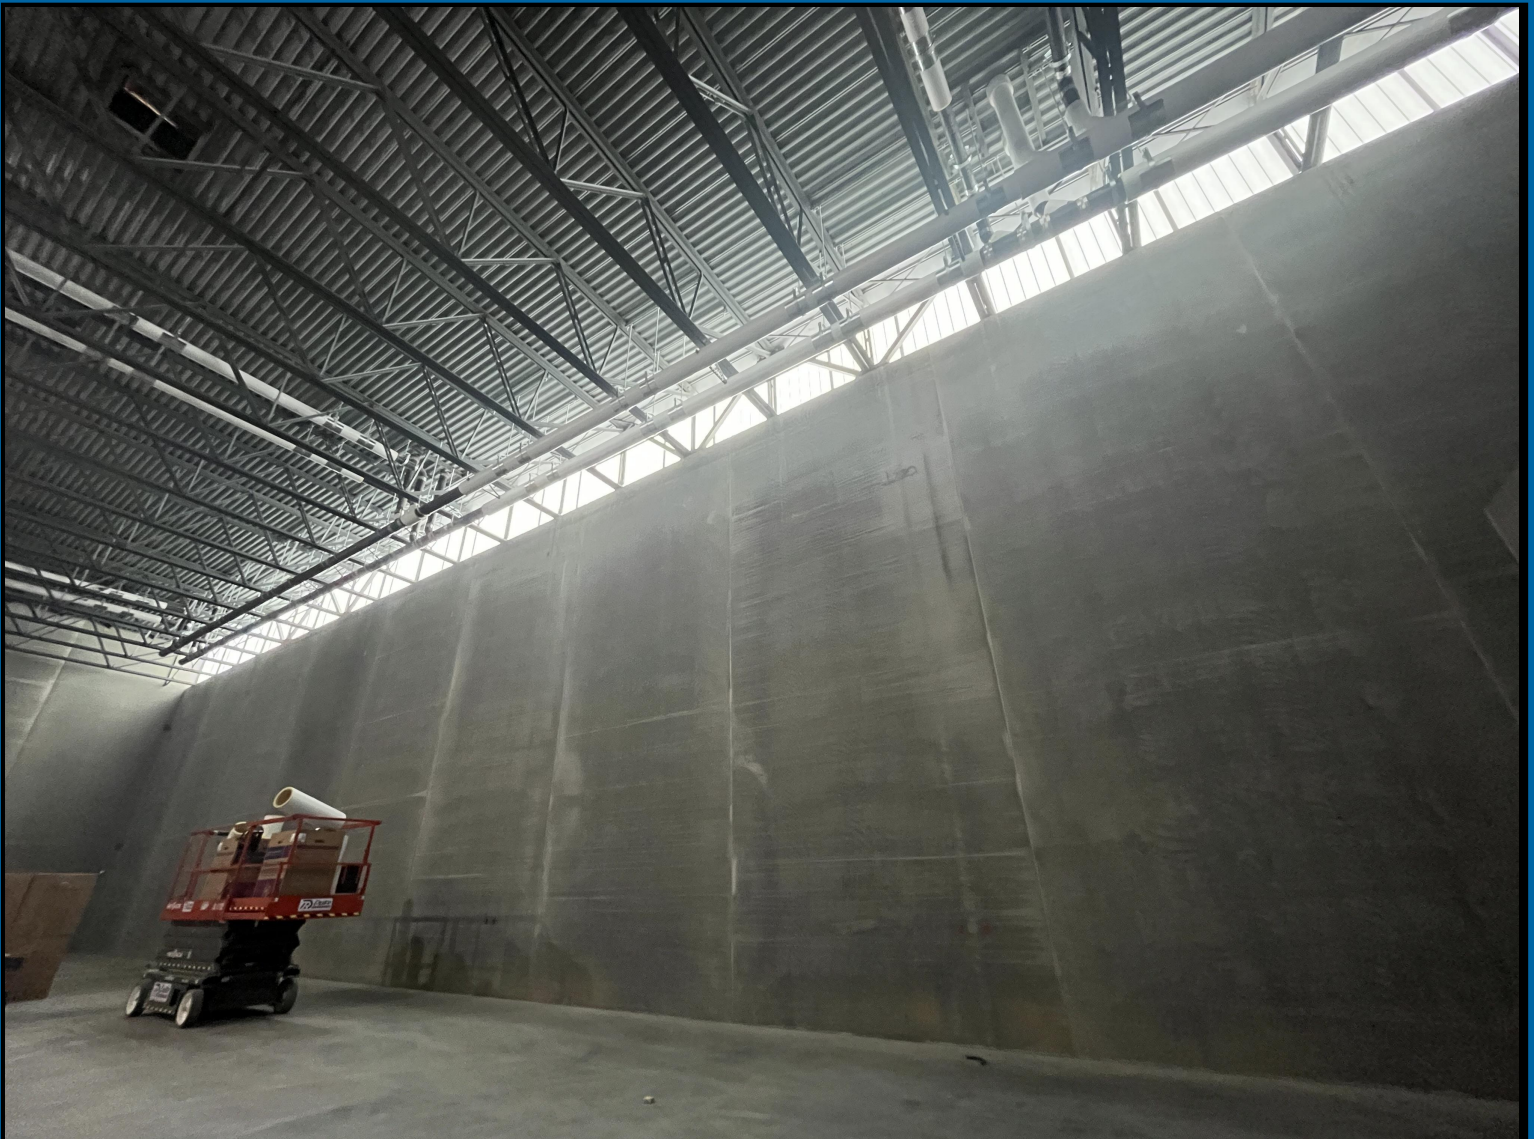

Commons Area Stairwell



2nd Floor Corridor/Commons



Typical 2nd Floor Classroom

